


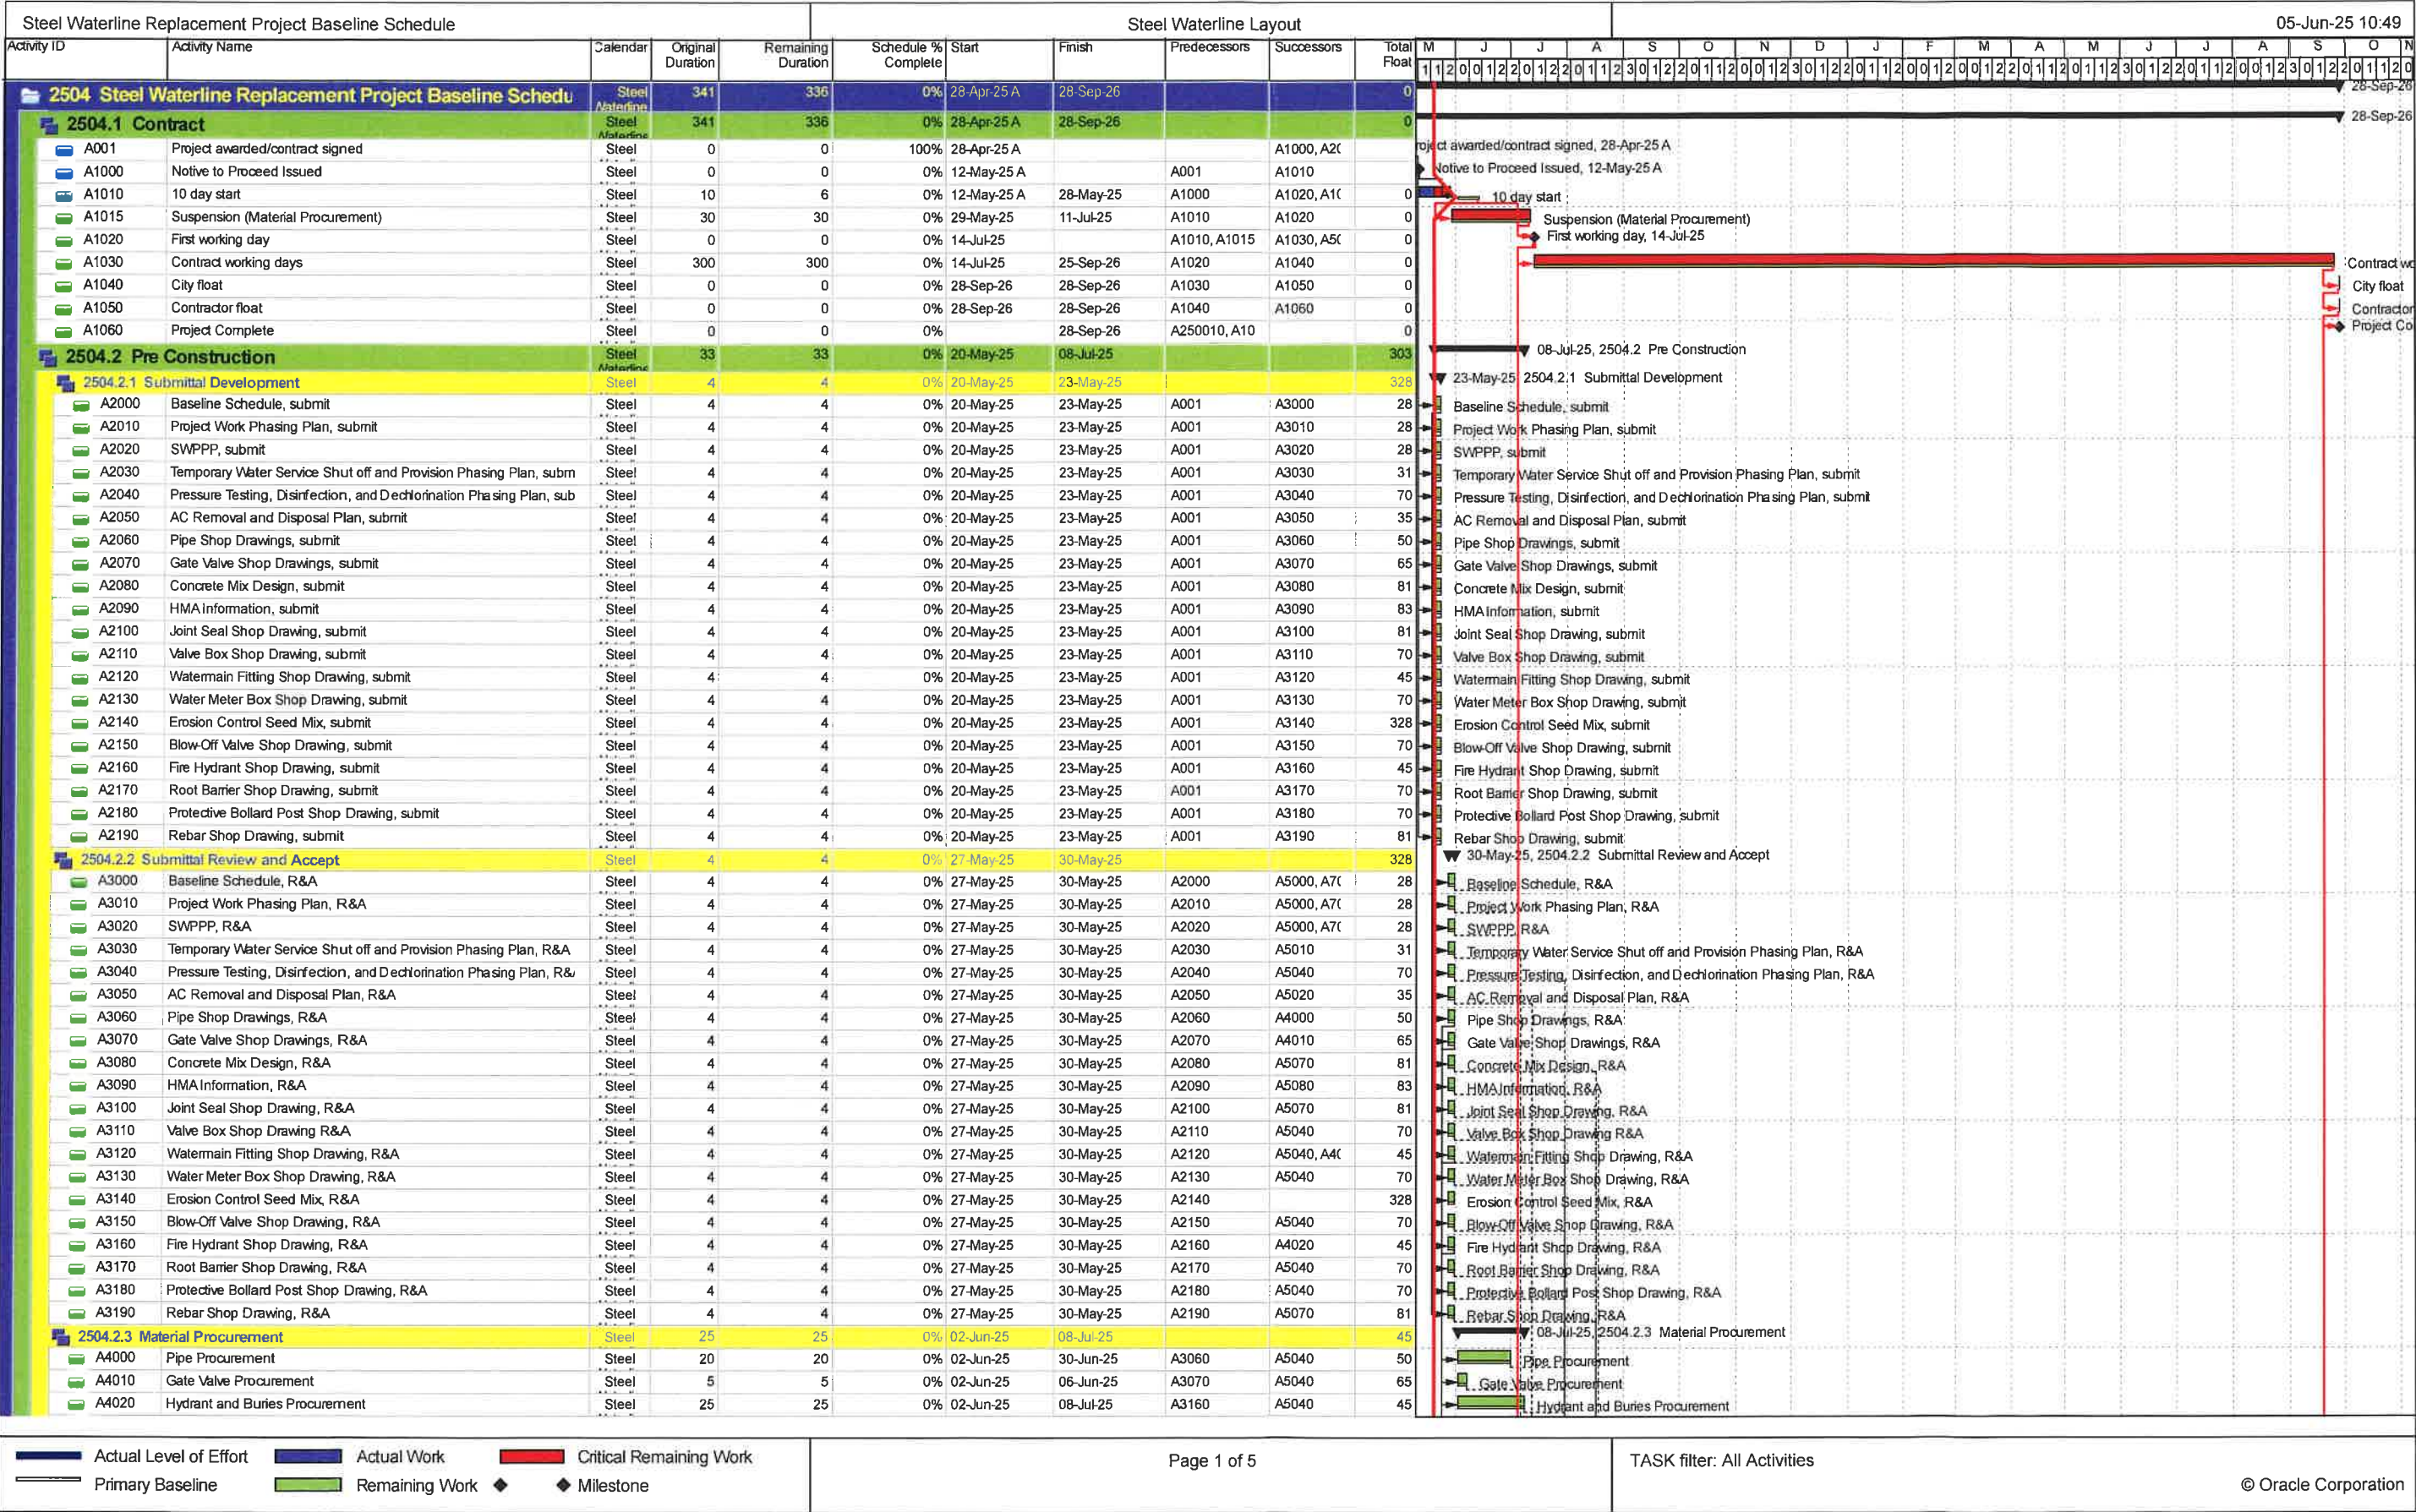

[illegible]

Steel Waterline Replacement Project Baseline Schedule							Steel Waterline Layout										05-Jun-25 10:49																											
Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Predecessors	Successors	Total Float	M	J	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N														
A11020	Saw cut existing asphalt/concrete	Steel	3	3	0%	04-Sep-25	08-Sep-25	A11010	A11030, A'	9																																		
A11030	Remove/replace existing infrastructure, trench and backfill, place cold patch	Steel	15	15	0%	18-Sep-25	08-Oct-25	A11020, A100	A11040, A'	2																																		
A11040	Install new water services	Steel	5	5	0%	09-Oct-25	16-Oct-25	A11030, A100	A11050	2																																		
A11050	Pressure test and chlorinate new mains and services	Steel	2	2	0%	17-Oct-25	20-Oct-25	A11040	A11060	2																																		
A11060	Restore permanent water service, backfill and outback street holes	Steel	4	4	0%	21-Oct-25	24-Oct-25	A11050	A11070, A'	2																																		
A11070	Replace sidewalk	Steel	2	2	0%	27-Oct-25	28-Oct-25	A11060, A100	A11080	2																																		
A11080	Patch pave streets	Steel	1	1	0%	29-Oct-25	29-Oct-25	A11070	A6005, A12	2																																		
2504.3.7 Plan Sheet C-108 Area - 1096 LF																																												
A12000	Notify residents of disturbance, setup traffic control	Steel	1	1	0%	07-Oct-25	07-Oct-25	A10080	A12010	0																																		
A12010	Install temporary water service, test and chlorinate	Steel	3	3	0%	08-Oct-25	10-Oct-25	A12000, A110	A12020	0																																		
A12020	Saw cut existing asphalt/concrete	Steel	2	2	0%	10-Oct-25	14-Oct-25	A12010	A12030, A'	0																																		
A12030	Remove/replace existing infrastructure, trench and backfill, place cold patch	Steel	10	10	0%	15-Oct-25	28-Oct-25	A12020, A110	A12040, A'	0																																		
A12040	Install new water services	Steel	4	4	0%	29-Oct-25	03-Nov-25	A12030, A110	A12050	0																																		
A12050	Pressure test and chlorinate new mains and services	Steel	1	1	0%	04-Nov-25	04-Nov-25	A12040	A12060	0																																		
A12060	Restore permanent water service, backfill and outback street holes	Steel	5	5	0%	05-Nov-25	12-Nov-25	A12050	A12070, A'	0																																		
A12070	Replace sidewalk	Steel	3	3	0%	13-Nov-25	17-Nov-25	A12060, A110	A12080	0																																		
A12080	Patch Pave Streets	Steel	1	1	0%	18-Nov-25	18-Nov-25	A12070, A100	A13000, A'	0																																		
2504.3.8 Plan Sheet C-109 (Ross St) Area - 532 LF																																												
A6005	Notify residents of disturbance, setup traffic control	Steel	1	1	0%	30-Oct-25	30-Oct-25	A11080	A6010	2																																		
A6010	Install temporary water service, test and chlorinate	Steel	2	2	0%	31-Oct-25	03-Nov-25	A6005, A12020	A6020	2																																		
A6020	Saw cut existing asphalt/concrete	Steel	1	1	0%	03-Nov-25	03-Nov-25	A6010	A6030, A12	2																																		
A6030	Remove/replace existing infrastructure, trench and backfill, place cold patch	Steel	7	7	0%	04-Nov-25	13-Nov-25	A6020, A8030	A6040, A12	2																																		
A6040	Install new water services	Steel	2	2	0%	14-Nov-25	17-Nov-25	A6030, A12060	A6050	2																																		
A6050	Pressure test and chlorinate new mains and services	Steel	1	1	0%	18-Nov-25	18-Nov-25	A6040	A6060	2																																		
A6060	Restore permanent water service, backfill and outback street holes	Steel	1	1	0%	19-Nov-25	19-Nov-25	A6050	A6070, A12	2																																		
A6070	Replace sidewalk	Steel	1	1	0%	20-Nov-25	20-Nov-25	A6060	A6080	2																																		
A6080	Patch pave streets	Steel	1	1	0%	21-Nov-25	21-Nov-25	A6070	A14000, A'	2																																		
2504.3.9 Plan Sheet C-109 (14th Street) Area - 288 LF																																												
A13000	Notify residents of disturbance, setup traffic control	Steel	1	1	0%	19-Nov-25	19-Nov-25	A12080	A13010	0																																		
A13010	Install temporary water service, test and chlorinate	Steel	2	2	0%	20-Nov-25	21-Nov-25	A13000, A6020	A13020	0																																		
A13020	Saw cut existing asphalt/concrete	Steel	1	1	0%	21-Nov-25	21-Nov-25	A13010	A13030, A'	0																																		
A13030	Remove/replace existing infrastructure, trench and backfill, place cold patch	Steel	4	4	0%	24-Nov-25	01-Dec-25	A13020, A6030	A13040, A'	0																																		
A13040	Install new water services	Steel	1	1	0%	02-Dec-25	02-Dec-25	A13030, A6060	A13050	0																																		
A13050	Pressure test and chlorinate new mains and services	Steel	1	1	0%	03-Dec-25	03-Dec-25	A13040	A13060	0																																		
A13060	Restore permanent water service, backfill and outback street holes	Steel	1	1	0%	04-Dec-25	04-Dec-25	A13050	A13070, A'	0																																		
A13070	Replace sidewalk	Steel	1	1	0%	05-Dec-25	05-Dec-25	A13060, A6080	A13080	0																																		
A13080	Grind and Pave Streets	Steel	1	1	0%	08-Dec-25	08-Dec-25	A13070, A608	A15000	0																																		
2504.3.10 Plan Sheet C-110 (15th St and L St) Area - 695 LF																																												
A14000	Notify residents of disturbance, setup traffic control	Steel	1	1	0%	24-Nov-25	24-Nov-25	A6080	A14010	2																																		
A14010	Install temporary water service, test and chlorinate	Steel	3	3	0%	25-Nov-25	01-Dec-25	A14000, A130	A14020	2																																		
A14020	Saw cut existing asphalt/concrete	Steel	2	2	0%	01-Dec-25	02-Dec-25	A14010	A14030, A'	2																																		
A14030	Remove/replace existing infrastructure, trench and backfill, place cold patch	Steel	8	8	0%	03-Dec-25	12-Dec-25	A14020, A130	A14040, A'	2																																		
A14040	Install new water services	Steel	3	3	0%	15-Dec-25	17-Dec-25	A14030, A130	A14050	2																																		
A14050	Pressure test and chlorinate new mains and services	Steel	2	2	0%	18-Dec-25	19-Dec-25	A14040	A14060	2																																		
A14060	Restore permanent water service, backfill and outback street holes	Steel	2	2	0%	22-Dec-25	23-Dec-25	A14050	A14070, A'	2																																		
A14070	Replace sidewalk	Steel	1	1	0%	24-Dec-25	24-Dec-25	A14060, A8090	A14080	2																																		
A14080	Patch Pave Streets	Steel	1	1	0%	29-Dec-25	29-Dec-25	A14070	A16000, A'	2																																		
2504.3.11 Plan Sheet C-110, C-111, C-112 (J St for all) Area - 1526 LF																																												
A15000	Notify residents of disturbance, setup traffic control	Steel	1	1	0%	09-Dec-25	09-Dec-25	A13080	A15010	0																																		
A15010	Install temporary water service, test and chlorinate	Steel	3	3	0%	10-Dec-25	12-Dec-25	A15000, A140	A15020	0																																		
A15020	Saw cut existing asphalt/concrete	Steel	3	3	0%	12-Dec-25	16-Dec-25	A15010	A15030, A'	0																																		
A15030	Remove/replace existing infrastructure, trench and backfill, place cold patch	Steel	15	15	0%	17-Dec-25	12-Jan-26	A15020, A120	A15040, A'	0																																		
A15040	Install new water services	Steel	4	4	0%	13-Jan-26	16-Jan-26	A15030, A120	A15050	0																																		
A15050	Pressure test and chlorinate new mains and services	Steel	2	2	0%	20-Jan-26	21-Jan-26	A15040	A15060	0																																		
A15060	Restore permanent water service, backfill and outback street holes	Steel	5	5	0%	22-Jan-26	28-Jan-26	A15050	A15070, A'	0																																		
A15070	Replace sidewalk	Steel	2	2	0%	29-Jan-26	30-Jan-26	A15060, A120	A15080	4																																		
A15080	Patch pave streets	Steel	1	1	0%	02-Feb-26	02-Feb-26	A15070	A16070, A'	4																																		
2504.3.12 Plan Sheet C-111, C-112 (K St for all) Area - 940 LF																																												
A16000	Notify residents of disturbance, setup traffic control	Steel	1	1	0%	30-Dec-25	30-Dec-25	A14080	A16010	2																																		

Actual Level of Effort

Primary Baseline

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Page 3 of 5

TASK filter: All Activities

© Oracle Corporation

